


ID	Task Mode	Task Name	Duration	Start	Finish	Timeline																														
						July	August	September	October	November	December	January	February	March																						
1		Order reception	0 days	Wed 13/04/16	Wed 13/04/16																															
2	✓	Kick-Off preparation	4 wks	Wed 13/04/16	Tue 10/05/16																															
3	✓	Kick-Off Meeting	0 days	Tue 10/05/16	Tue 10/05/16																															
4	✓	Design clarification by CERN	6 wks	Wed 13/04/16	Tue 24/05/16																															
5	✓	Design update by ACS	3 wks	Wed 13/04/16	Tue 03/05/16																															
6	✓	Double heater W580	130 days	Mon 30/05/16	Fri 06/01/17																															
14		Cryostat Gersemi	247 days	Mon 20/06/16	Wed 19/07/17																															
15	✓	Manufacturing drawings	24 wks	Wed 13/07/16	Tue 07/02/17																															
16	✓	Uppsala drawings acceptance	0 days	Tue 21/02/17	Tue 21/02/17																															
17	✓	Manufacturing procedures	3 wks	Wed 22/02/17	Tue 14/03/17																															
18		Procurement	200 days	Mon 20/06/16	Wed 10/05/17																															
23		Manufacturing	130 days	Wed 11/01/17	Wed 19/07/17																															
24	✓	Lambda seat flange pre-machining	8 wks	Wed 11/01/17	Tue 07/03/17																															
25	✓	Lambda seat flange welding	4 wks	Wed 08/03/17	Tue 04/04/17																															
26	✓	Lambda seat flange final machining	4 wks	Wed 05/04/17	Thu 04/05/17																															
27	✓	Dewar welding	3 wks	Fri 05/05/17	Tue 30/05/17																															
28		Dewar welding to top flange	1 wk	Wed 07/06/17	Tue 13/06/17																															
29		Dewar piping and equipment	4 wks	Wed 14/06/17	Tue 11/07/17																															
30		Screens manufacturing	4 wks	Mon 22/05/17	Tue 20/06/17																															
31		Dewar insertion in vacuum vessel	1 wk	Wed 12/07/17	Wed 19/07/17																															
32		Magnet insert	195 days	Thu 23/02/17	Thu 21/12/17																															
33	✓	Manufacturing drawings	18 wks	Thu 23/02/17	Wed 05/07/17																															
34		Manufacturing procedures	3 wks	Thu 06/07/17	Thu 27/07/17																															
35		Uppsala drawings acceptance	0 days	Thu 31/08/17	Thu 31/08/17																															
36		Procurement	2 mons	Fri 01/09/17	Thu 26/10/17																															
37		Manufacturing	12 wks	Fri 29/09/17	Thu 21/12/17																															
38	✓	Bath insert	125 days	Mon 29/08/16	Wed 08/03/17																															
44		Valves box GERSEMI	258 days	Mon 20/06/16	Thu 03/08/17																															
45	✓	Manufacturing drawings	12 wks	Mon 05/09/16	Wed 30/11/16																															
46	✓	Valves box design review	0 days	Wed 07/12/16	Wed 07/12/16																															
47	✓	Manufacturing procedures	3 wks	Thu 13/04/17	Fri 05/05/17																															
48	✓	Procurement	170 days	Mon 20/06/16	Fri 24/03/17																															
53		Manufacturing	12 wks	Tue 09/05/17	Thu 03/08/17																															
54		Transfer lines design&manufacturing	90 days	Thu 06/04/17	Thu 07/09/17																															

Project: 2017-07-05 - Gersemi
Date: Sun 09/07/17

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

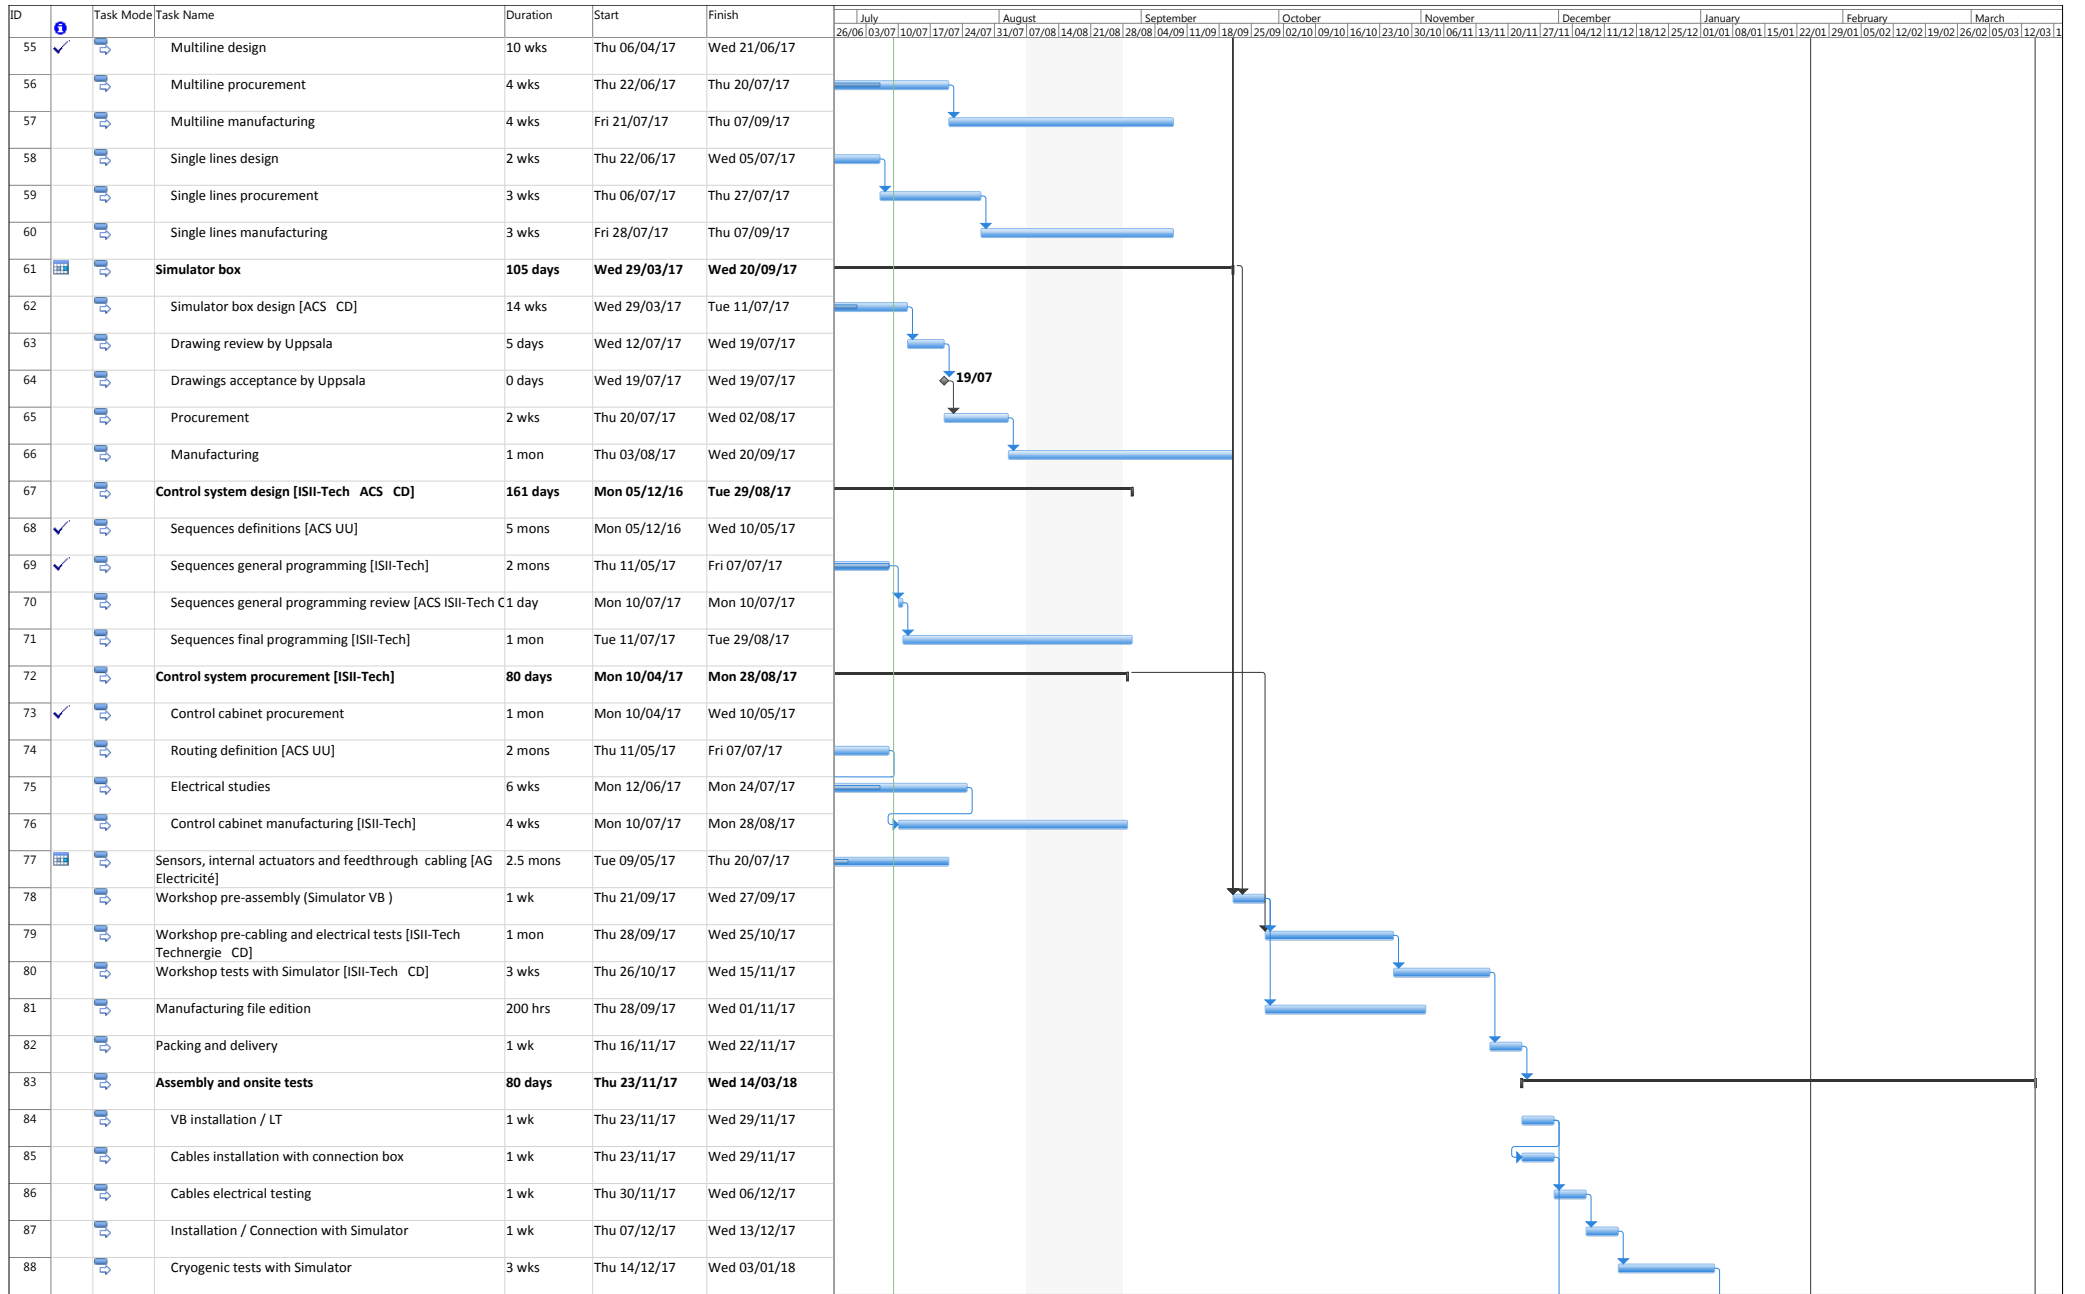

Project: 2017-07-05 - Gerserni
Date: Sun 09/07/17

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

