ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1			Order reception	0 days	Wed 13/04/16	Wed 13/04/16		
2	✓		Kick-Off preparation	4 wks	Wed 13/04/16	Tue 10/05/16	1	
3	✓		Kick-Off Meeting	0 days	Tue 10/05/16	Tue 10/05/16	2	
4	✓		Design clarification by CERN	6 wks	Wed 13/04/16	Tue 24/05/16		
5	✓		Design update by ACS	3 wks	Wed 13/04/16	Tue 03/05/16		
6	✓		**Double heater WS80**	**130 days**	**Mon 30/05/16**	**Fri 06/01/17**	**3**	
14			**Cryostat Gersemi**	**247 days**	**Mon 20/06/16**	**Wed 19/07/17**	**3**	
32			**Magnet insert**	**195 days**	**Thu 23/02/17**	**Thu 21/12/17**		
38	✓		**Bath insert**	**125 days**	**Mon 29/08/16**	**Wed 08/03/17**		
44			**Valves box GERSEMI**	**258 days**	**Mon 20/06/16**	**Thu 03/08/17**		
54			**Transfer lines design&manufacturing**	**90 days**	**Thu 06/04/17**	**Thu 07/09/17**	**7,15FS-1 mon,33FS-3 mons,39,45**	
61			**Simulator box**	**105 days**	**Wed 29/03/17**	**Wed 20/09/17**		
67			**Control system design [ISII-Tech ACS CD]**	**161 days**	**Mon 05/12/16**	**Tue 29/08/17**		
72			**Control system procurement [ISII-Tech]**	**80 days**	**Mon 10/04/17**	**Mon 28/08/17**		
77			Sensors, internal actuators and feedthrough cabling [AG Electricité]	2.5 mons	Tue 09/05/17	Thu 20/07/17		
78			Workshop pre-assembly (Simulator VB)	1 wk	Thu 21/09/17	Wed 27/09/17	14,38,44,54FS-1 mon,61	
79			Workshop pre-cabling and electrical tests [ISII-Tech Technergie CD]	1 mon	Thu 28/09/17	Wed 25/10/17	72,78	
80			Workshop tests with Simulator [ISII-Tech CD]	3 wks	Thu 26/10/17	Wed 15/11/17	79	
81			Manufacturing file edition	200 hrs	Thu 28/09/17	Wed 01/11/17	78	
82			Packing and delivery	1 wk	Thu 16/11/17	Wed 22/11/17	80	
83			**Assembly and onsite tests**	**80 days**	**Thu 23/11/17**	**Wed 14/03/18**	**82**	

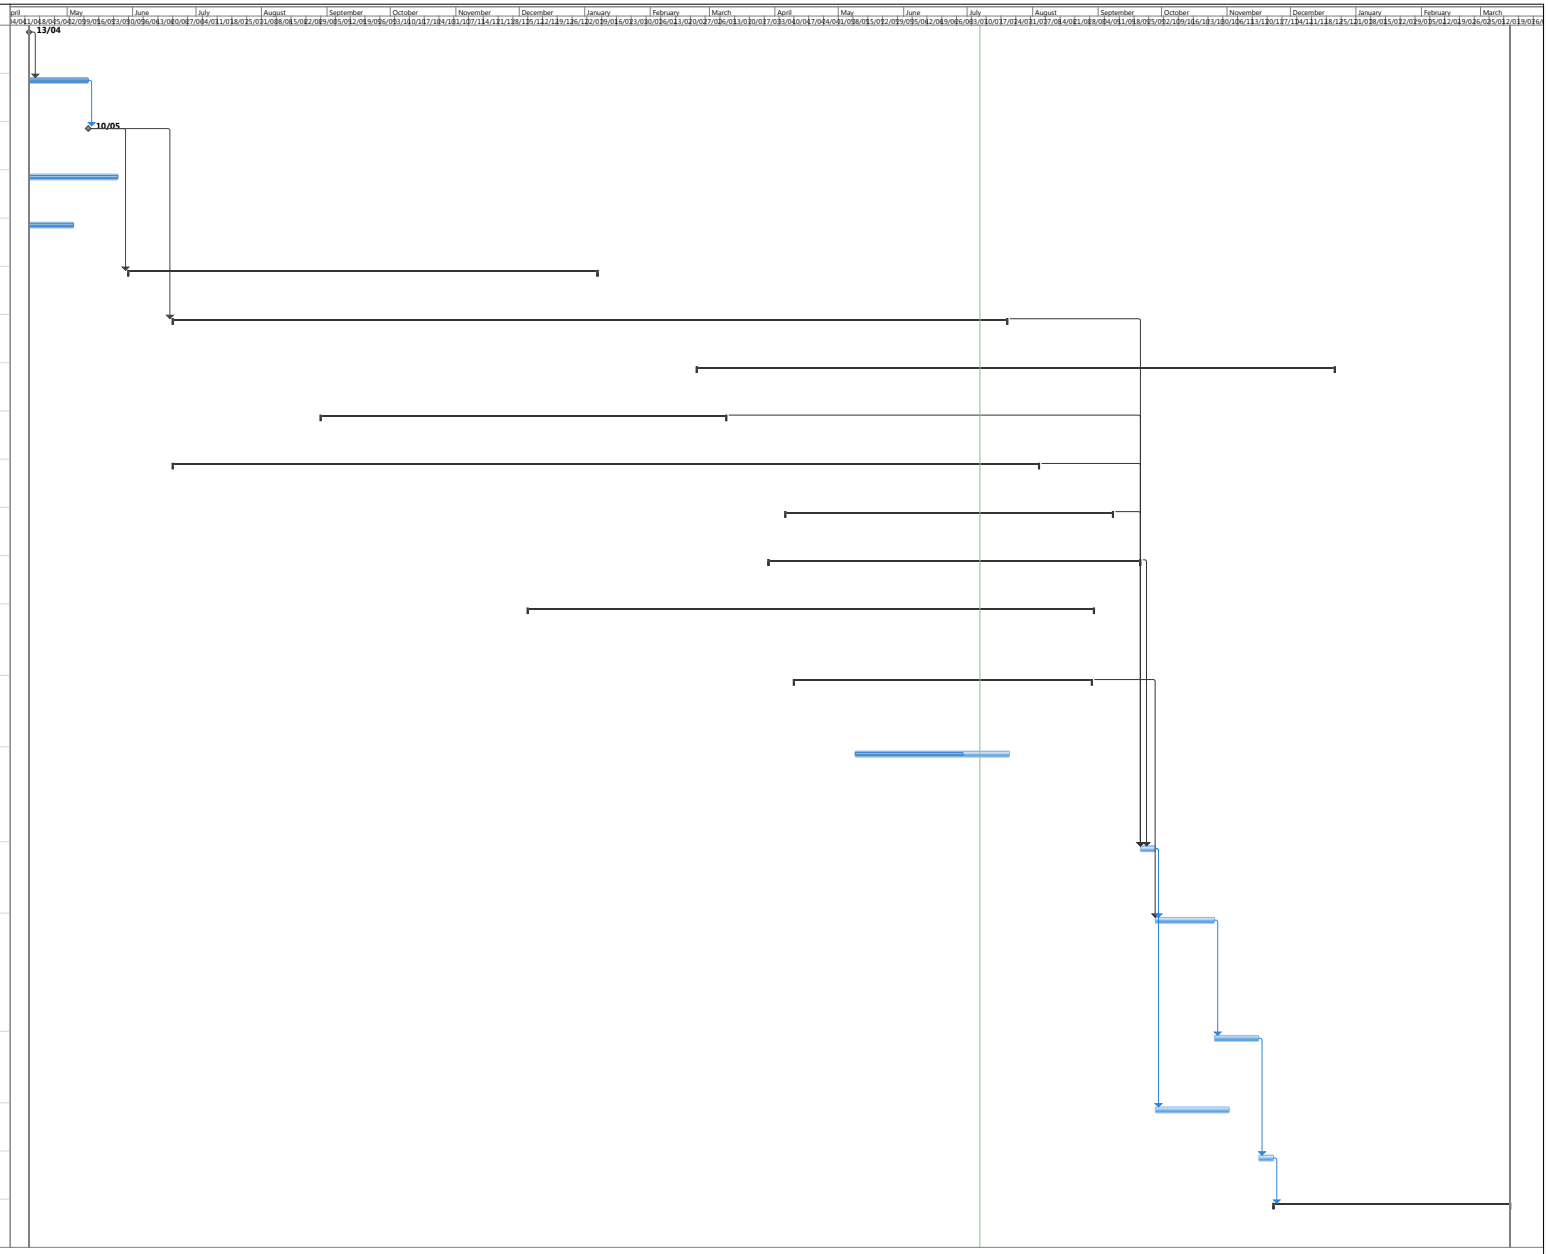

Project: 2017-07-05 - -Gersemi
Date: Fri 07/07/17

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
